

Before the National Green Tribunal

SOUTHERN ZONE, CHENNAI

**Execution Application No.11 of 2023 (SZ) in
Original Application No.523 of 2018 (PB)**

WITH

Original Application No.127 of 2022 (SZ)

WITH

Original Application No.156 of 2024 (SZ)



**DETAILED STATUS REPORT AND WORKABLE PLAN OF
ACTION FOR HANDLING LEGACY WASTE AND
ACHIEVING ZERO FRESH DUMPING AT VELLALORE
FILED BY THE COIMBATORE CITY MUNICIPAL
CORPORATION**

NAJEEB USMAN KHAN

Counsel for 1st Respondent

Cell : 98400 33766

Before the National Green Tribunal

SOUTHERN ZONE, CHENNAI

Execution Application No.11 of 2023 (SZ) in

Original Application No.523 of 2018(PB)

WITH

Original Application No.127 of 2022 (SZ)

WITH


Original Application No.156 of 2024 (SZ)

INDEX

Sl. No.	Particulars	Annexure	Page No.
	Current status Report in support of Status Report of the Initiative taken by 1 st Respondent – Municipal Corporation of Coimbatore dated : 01.09.2024		1
1	Committee appointed by Commissioner to monitor the processing facilities at the Vellalore Compost yard <i>with translation</i>	R-I	7
2	Site inspection on 22nd December 2024 by Commissioner	R-II	18
3	Show Cause notices to all service providers in Vellalore Compost Yard	R-III	19

4	Action taken photographs by the service providers after the receipt of Show Cause Notice like spraying of disinfectant and Lemon grass solutions.	R-IV	29
5	Photographs of about 3000 saplings in the compost yard and the inside of the compost plant area	R-V	30
6	Copies of the spraying Lemon Grass solution spanning about 60acre	R-VI	31
7	A copy of the letter dated 09.12.2024 imposing penalty of Rs. 50,00,000 on the concessionaire (SPV)	R-VII	34
8	A copy of the Tender notice of Phase II of the Bio-Mining about 7.43 Lakhs MT of legacy waste	R-VIII	36
9	News item appearing in Dinakaran daily Coimbatore edition dated - 07.01.2025 for Solar Panel Project to be implemented in the reclaimed 50 acres of land	R-IX	37
10	Photographs of the under construction Revamped Sathy Road Transfer Station	R-X	38
11	Copy of Letter of Acceptance construction of three new transfer stations	R-XI (Colly)	39
12	Copy of the notice from the Hon'ble High Court of Madras at Chennai	R-XII	42
13	Table showing Percentage of Open dumping and Processed waste in Vellalore compost yard	R-XIII	46

Dated: 15.02.2025


Advocate for Respondent No.1

BEFORE THE NATIONAL GREEN TRIBUNAL
SOUTHERN ZONE, CHENNAI

Execution Application No.11 of 2023 (SZ) in
Original Application No.523 of 2018(PB)

WITH

Original Application No.127 of 2022 (SZ)

WITH

Original Application No.156 of 2024 (SZ)

IN THE MATTER OF:

V. Eswaran, Coimbatore. ... Applicant(s)

Versus

The District Collector, Coimbatore District and Anr. ...Respondent(s)

WITH

K.S. Mohan, Coimbatore. ...Applicant(s)

Versus

The Corporation of Coimbatore

Represented by its Commissioner Coimbatore and Ors.

...Respondent(s)

WITH

Tribunal on its own motion SUO MOTU based on

the news item published in 'The Hindu' dated 07.04.2024,

titled "Fire breaks out at Vellalore landfill in Coimbatore"

And Central Pollution Control Board

Through its Member Secretary, New Delhi and Ors. ...

...Respondent(s)

CURRENT STATUS REPORT REGARDING THE STEPS TAKEN WITHIN THE LAST THREE (3) MONTHS OF THE PREVIOUS STATUS REPORT BY THE COIMBATORE CITY MUNICIPAL CORPORATION DATED 01.09.2024

This Additional Affidavit to the Status Report is filed on behalf of the Respondent-Coimbatore City Municipal Corporation (CCMC) through the Commissioner Mr. M. Sivaguru Prabakaran, IAS to outline the ongoing initiatives and progress made to address Municipal Solid Waste (MSW) management, legacy waste bio-mining, to avoid open dumping at the Vellalore Dump Yard and the Odor issue along with the initiative taken for implementing new project proposals. The report reflects the Coimbatore City Municipal Corporation's commitment to managing municipal solid waste, implementing sustainable solutions, and eliminating open dumping at the Vellalore yard. All relevant annexures have been attached for reference.

1. The Coimbatore City Municipal Corporation has formed a Solid Waste Management Committee, chaired by the Deputy Commissioner and comprising 14 members (including Engineers, Assistant Commissioner and Sanitary Officers from all the zones). This committee oversees solid waste management operations at the compost plant, including:

The appointed Private Service Provider (PSP) collects waste daily and transport it to transfer stations at Ukkadam and Peelamedu. From there, waste is moved to the Vellalore Compost Yard using compactor bins from M/s. Coimbatore Integrated Waste Management Co. Pvt. Ltd. (CIWMCPL).

The Committee shall monitor & supervise the following Contractor's obligations:

- Vehicle waiting times and delays at transfer stations.
- The number of operational vehicles transporting solid waste.

- The daily quantity of solid waste transported.
- Availability of bins for waste collection.
- Accuracy of weight measurements and weighing machine licenses.
- Ensure that the daily waste supplied is processed
- Ensure that the weight of RDF material sent to cement factory.
- After composting ensure that all the Rejects and Inert are sent to Sanitary Landfill
- Leachate from SLF is treated or not on a regular basis
- Certify that the 'Fit for Landfill certificate' is issued in accordance to SWM Rules,2016
- Ensure that the processing activities are followed as per MSW Rules and Act,2016
- Composting methods for wet waste.
- The ratio of segregated and processed waste to be maintained.
- Processing methods for wet and dry waste.
- Sales of compost and Refuse-Derived Fuel (RDF) particulars.
- Maintenance frequencies of transfer station equipment.
- Procedures for environmental protection as per regulations.

Similarly, a Committee has been formed to monitor the Vermi Compost Committee under the Chairmanship of the Deputy Commissioner and consists of 17 officials (including Engineers, Assistant Commissioner and ZSO of all Zones) from CCMC to oversee the work of preparation of vermi compost plant which is currently underway. The current implementation process is under review, and amendments have been ordered.

The officials mentioned above shall inspect whether the vermicomposting production at the Vellalore dump yard is being conducted properly. They will also examine the list of expenses incurred for the vermicomposting production work recorded and submit a

report to the Commissioner through the Deputy Commissioner. Copy of the proceedings is produced herewith as **Annexure- R-1**

2. The Commissioner and the Solid Waste Committee conducted a joint site inspection on December 22, 2024, and noted all instances of non-compliance by the appointed service providers. The site inspection photographs are enclosed as **Annexure – R-2**.
3. The Committee met on 23rd December 2024 after evaluation of the onsite progress made by various contractors appointed under the Municipal Solid Waste Management has pointed out irregularities regarding odor and therefore issued show cause notices to all service providers working inside Vellalore Compost Yard to stop operation after 6 p.m. to 6 a.m. (night time) and to process the daily received waste on the same day, further directing the service providers for installation of CCTV surveillance, appointment of additional CCMC supervisors and to take necessary action of spraying of disinfectant and lemon grass solution to mitigate odor issues. Copy of the Show Cause Notices issued to the service providers are in **Annexure R-3(Colly)**
4. Action taken by the service providers like spraying of disinfectant and Lemon grass solutions in processing plant area is shown in the photographs produced as in **Annexure –R-4**
5. As part of the mitigating the odor issues, CCMC has planted about 3000 saplings in the compost yard and inside the compost plant area. Plantation photographs are produced herewith as **Annexure R-5**.
6. CCMC has taken initiatives to spray solutions using drones, spanning about 65 acres where the old/fresh waste was dumped to mitigate odor issues, the photographs of the drone spraying in the Vellalore Compost yard and the Google map of the area covered by drone spraying is produced here as **Annexure R-6**
7. CCMC has imposed penalty of Rs.50,00,000 (Rupees Fifty Lacs) on the service provider M/s CIWMCPL for the discharge of untreated Leachate flowing out from the boundary wall which had accumulated in the neighboring property due to improper maintenance of the Leachate Treatment Plant in the concessionaire's compost yard, which was one of the obligations under the concession Agreement

with the Concessionaire. A copy of the letter dated 09.12.2024 imposing penalty on the concessionaire (SPV) is produced here as **Annexure R-7**

8. Under the Phase II of the Bio-Mining about 7.43 Lakhs MT of legacy waste will be cleared for which tender is called and it will be opened on 28.01.2025. CCMC shall finalize the bidder and start the operations of Phase II tentatively from March 2025. Approximately, 84.62 acres will be reclaimed after the bio-mining process is completed. A copy of the Tender notice is produced herewith as **Annexure R-8**
9. CCMC is setting up to install the Solar Panel Project in the reclaimed 54 acres of land and DPR is being prepared. The article covering the news item of Solar Panel Project at Vellalore in Dinamalar Daily, Coimbatore Edition dated 7th January, 2025 is produced as **Annexure R-9**. The Solar Panel Project is estimated at a whopping 150 crore rupees estimate, to set up a 20 MW (megawatt) solar power plant to be established in Vellalore. By this CCMC ensures to stop Open dumping at Vellalore and a sustainable long term revenue generation project will be initiated.
10. It is respectfully submitted that the Respondent Corporation in support of their submissions in Page 8 of the Detailed Status Report and Workable Plan of Handling Legacy Waste and achieving Zero Fresh waste dumping at Vellalore the Construction Work Revamp of Sathy Road Transfer Station will be completed in April'25 having capacity of 150 TPD. After the completion of the construction and functional it would still reduce open dumping at Vellalore Yard. Photographs of the under construction Revamped Sathy Road Transfer Station is produced as **Annexure R-10**.
11. The construction of three new transfer stations at Kovaipudur, Peelamedu and Kavundapalayam of 200 TPD capacity each will be commenced shortly. The completion period is 12 months and this will help CCMC to channelize the municipal solid wastes to different processing facilities and to control sending the wastes to the open dumping at Vellalore compost yard. Copy of Letter of Acceptance dated 31.12.2024 is enclosed as in **Annexure R-11 (Colly)**
12. Construction of Bio-CNG plant of 250 TPD, at an estimate of Rs.69.20 crore for 'Biogas' project for which tender is floated on 13.12.2024, One of the bidder filed a case before the Hon'ble High Court as W.P 38606 of 2024 and this Respondent has appeared on notice from the Hon'ble High Court of Madras at Chennai. Matter has been adjourned to 03.02.2025 which is produced as **Annexure R-12** and the

judgement in the above matter is on 21st January, 2025. After the judgement, CCMC shall finalize the bidder and work order shall be issued. Tentative commencement of the project shall be April'25 and the completion period is 12months from the commencement date. Setting up of the plant shall assist CCMC in controlling the open dumping at Vellalore compost yard.


13. A plan to implementation of Waste to Energy Plant of 600 metric tons of garbage shall be implemented. It will be implemented in collaboration with local self-governing bodies near the municipality. The detailed project report is in progress and would be initiated shortly. With the implementation of the biogas production project and the electricity generation project, garbage can be diverted from the landfill.

14. CCMC has taken the initiative to reduce open dumping by a great margin as seen in **Annexure R-13** that the segregation percentage since November 2023 till December 2024 has drastically reduced from 36% to 14% where as the processing waste quantity increased from 64% to 86%


For the foregoing reasons it is most humbly prayed that the current status report be accepted and pass appropriate orders as it deems fit and necessary in the facts and circumstance of the case.

All facts stated above is true and correct

Dated 15.02.2025
Coimbatore


Deponent

COMMISSIONER
COIMBATORE CORPORATION


Counsel for the Respondent

கோயம்புத்தூர் மாநகராட்சி ஆணையர் அவர்களின் செயல்முறை ஆணைகள்

முன்னிலை: திரு.மா.சிவகுரு பிரபாகரன், இ.ஆ.ப.,

திருவள்ளூர் ஆண்டு 2055 / குரோதி / கார்த்திகை - 26

ந.க.எண்.2185/2024/எம்.சி.3

நாள்.11.12.2024

பொருள்: பணியமைப்பு - கோயம்புத்தூர் மாநகராட்சி - வெள்ளலூர் உரக்கிடங்கில் இயங்கிவரும் மண்புழு உரம் தயாரிக்கும் பணியை ஆய்வு மேற்கொண்டு - அறிக்கை சமர்ப்பிக்க அலுவலர்களுக்கு பணி ஒதுக்கீடு செய்து திருத்திய ஆணை பிறப்பித்தல் - தொடர்பாக.

பார்வை: இவ்வலுவலக இதே எண்ணிட்ட செயல்முறை ஆணை நாள்.02.12.2024.

ஆணை

கோயம்புத்தூர் மாநகராட்சி பகுதிகளில் சேகரமாகும் குப்பைகளை தரம் பிரித்து வெள்ளலூர் உரக்கிடங்கில் மண்புழு உரம் தயாரிக்கும் பணி (VERMI COMPOST) நடைபெற்று வருகிறது. இப்பணியினை கண்காணிக்கும் பொருட்டு துணை ஆணையர் அவர்களின் தலைமையில் குழு அமைத்து (VERMI COMPOST COMMITTEE) பார்வையில் கண்டுள்ளவாறு ஆணையிடப்பட்டது. தற்போது பார்வையில் காணும் செயல்முறை ஆணையினை திருத்தம் செய்து ஆணையிடப்படுகிறது.

வ.எண்.	பெயர் மற்றும் பதவி திரு / திருமதி / மரு.	தொலைபேசி எண்
1.	க.சிவகுமார், துணை ஆணையர்	7418920777
2.	ஜி.இளங்கோவன், துணை மாநகரப்பொறியாளர்	9443799211
3.	ஜி. முருகேசன், தலைமைப் பொறியாளர்(பொ)	9894674574
4.	ஏ.மோகன், நகர் நல அலுவலர்	9443799202
5.	க.பூபதி, உதவி நகர் நல அலுவலர்	9442104124
6.	என்.ஸ்ரீதேவி, உதவி ஆணையர், வடக்கு மண்டலம்	9489206045
7.	க.முத்துசாமி, உதவி ஆணையர், கிழக்கு மண்டலம்	9443799207
8.	து.சு.துரைமுருகன், உதவி ஆணையர், மேற்கு மண்டலம்	9489206055
9.	சி.செந்தில்குமரன், உதவி ஆணையர், மத்திய மண்டலம்	9443799236
10.	என்.குமரன், உதவி ஆணையர், தெற்கு மண்டலம்	9443799212
11.	வீரன், துப்புரவு அலுவலர், மேற்கு மண்டலம்	9443754100
12.	என்.இராஜேந்திரன், துப்புரவு அலுவலர், வடக்கு மண்டலம்	9443478727
13.	எஸ்.முருகன், துப்புரவு அலுவலர், கிழக்கு மண்டலம்	9865897150

14.	என்.விஜயகுமார், துப்புரவு அலுவலர், SBM	9442104137
15.	ஆர்.குணசேகரன், துப்புரவு அலுவலர்(பொ), மத்திய மண்டலம்	94421 04151
16.	எம்.வீ.ஆண்டியப்பன், துப்புரவு அலுவலர்(பொ) தெற்கு மண்டலம்	94421 04144
17.	எஸ்.ஜீவராஜ், உதவிப்பொறியாளர்	9489206015

மேற்குறிப்பிட்டுள்ள அலுவலர்கள் வெள்ளலூர் உரக்கிடங்கில் செயல்பட்டுவரும் மண்புழு உரம் தயாரிப்பு பணிகள் சரியான முறையில் செயல்படுத்தப்பட்டு வருகிறதா என்பதையும் மற்றும் மண்புழு உரம் தயாரிப்பு பணிகளுக்காக மேற்கொள்ளப்படும் செலவினங்கள் தொடர்பான அளவுப்புத்தக (M-Book) பட்டியலினை ஆய்வு மேற்கொண்டு அதன் அறிக்கையை துணை ஆணையர் வழியாக ஆணையர் அவர்களுக்கு சமர்ப்பிக்குமாறு ஆணையரிடமிருந்து.

ஆணையருக்காக,
துணை ஆணையர்,
கோயம்புத்தூர் மாநகராட்சி
10/12/2024

பெறுநர்

சம்பந்தப்பட்ட அனைத்து அலுவலர்கள்
கோயம்புத்தூர் மாநகராட்சி

கோயம்புத்தூர் மாநகராட்சி ஆணையர் அவர்களின் செயல்முறை ஆணைகள்
முன்னிலை: திரு.மா.சிவகுரு பிரபாகரன், இ.ஆ.ப.,

திருவள்ளூர் ஆண்டு 2055 / குரோதி / கார்த்திகை - 20

ந.க.எண்.415/2024/எம்சி7

நாள்.06.12.2024.

பொருள்: கோயம்புத்தூர் மாநகராட்சி - திடக்கழிவு மேலாண்மை திட்டம்-
மாநகராட்சி பகுதிகளில் தினசரி சேகரமாகும் திடக்கழிவுகளை
மேலாண்மை செய்யும் ஒப்பந்ததாரரான Concessionaire BEIL-UPL [SPV:
M/s. Coimbatore Integrated Waste Management Co. Pvt. Ltd. (CIWMCPL)]
என்ற நிறுவனம் மேற்கொள்ளும் பணியினை ஆய்வு மேற்கொண்டு
அறிக்கை சமர்ப்பிக்க (SOLID WASTE MANAGEMENT COMMITTEE) குழு
அமைத்து ஆணையரிடதுல் - தொடர்பாக.

ஆணை

கோயம்புத்தூர் மாநகராட்சி பகுதிகளில் தினசரி சேகரமாகும் திடக்கழிவுகளை
வாகனத்தின் மூலம் குப்பை மாற்று நிலையங்களுக்கு (Transfer Station)
கொண்டுசெல்லப்பட்டு, பின்பு குப்பை மாற்று நிலையங்களிலிருந்து லாரிகள் மூலம்
வெள்ளலூர் உரக்கிடங்கிற்கு கொண்டு செல்லப்பட்டு குப்பைகளை தரம் பிரிக்கும்
பணியினை Concessionaire BEIL-UPL [SPV: M/s. Coimbatore Integrated Waste Management Co.
Pvt. Ltd. (CIWMCPL)] என்ற நிறுவனம் மூலம் மேற்கொள்ளப்பட்டு வருகிறது.
இப்பணியினை கண்காணிக்கும் பொருட்டு துணை ஆணையர் அவர்களின்
தலைமையில் கீழ்க்கண்டவாறு (SOLID WASTE MANAGEMENT COMMITTEE) குழு அமைத்து
ஆணையரிடப்படுகிறது.


வ. எண்	பெயர் மற்றும் பதவி திரு / திருமதி / மரு.	தொலைபேசி எண்
1.	க.சிவகுமார், துணை ஆணையர்	7418920777
2.	ஜி.இளங்கோவன், துணை மாநகரப் பொறியாளர்	9443799211
3.	கே.கருப்புசாமி, செயற்பொறியாளர், மத்தியமண்டலம்	9443799219
4.	ஏ.மோகன், நகர் நல அலுவலர்	9443799202
5.	க.பூபதி, உதவி நகர் நல அலுவலர்	9442104124
6.	என்.குமரன், உதவி ஆணையர், தெற்கு மண்டலம்	9443799212
7.	ஆர்.எழில், உதவி செயற்பொறியாளர், வடக்கு மண்டலம்	9442501792
8.	எஸ்.கனகராஜ், உதவிசெயற்பொறியாளர் (பொ), தெற்கு மண்டலம்	9442501794
9.	சி.வீரன், சுகாதார அலுவலர், மேற்கு மண்டலம்	9443754100
10.	என்.இராஜேந்திரன், சுகாதார அலுவலர், வடக்கு மண்டலம்	9443478727
11.	எஸ்.முருகன், சுகாதார அலுவலர், கிழக்கு மண்டலம்	9865897150
12.	என்.விஜயகுமார், சுகாதார அலுவலர், SBM	9443111212
13.	ஆர்.குணசேகரன், சுகாதார அலுவலர் (பொ), மத்திய மண்டலம்	94421 04151
14.	எம்.வீ.ஆண்டியப்பன், சுகாதார அலுவலர் (பொ), தெற்குமண்டலம்	94421 04144

மேற்காண் அட்டவணையில் குறிப்பிட்டுள்ள அலுவலர்கள் கோயம்புத்தூர் மாநகராட்சி திடக்கழிவு மேலாண்மை பணிகளை மேற்கொண்டு வரும் Concessionaire BEIL-UPL [SPV: M/s. Coimbatore Integrated Waste Management Co. Pvt. Ltd. (CIWMCPL)] என்ற நிறுவனம் ஒப்பந்தத்தில் குறிப்பிட்டுள்ளவாறு திடக்கழிவு மேலாண்மை பணிகளை சரியான முறையில் செயல்படுத்தப்பட்டு வருகிறதா என்பதனை உதவிப்பொறியாளர், திடக்கழிவு மேலாண்மை, கோயம்புத்தூர் மாநகராட்சி மற்றும் M/S.InfraEn India Pvt Ltd, Coimbatore என்ற நிறுவனத்தினருடன் இணைந்து கீழ்க்கண்ட வீதங்களில் ஆய்வு மேற்கொண்டு இத்துடன் இணைக்கப்பட்ட படிவங்களில் பூர்த்தி செய்து தினசரி ஆய்வு அறிக்கையை ஒருங்கிணைத்து துணை ஆணையர் வழியாக ஆணையர் அவர்களுக்கு சமர்ப்பிக்குமாறு உத்தரவிடப்படுகிறது.

- குப்பை மாற்று நிலையங்களுக்கு (Transfer Station) வரும் வாகனங்களின் காத்திருக்கும் நேரம் மற்றும் அதற்கான காரணங்களை ஆய்வு செய்தல்.
- குப்பை மாற்று நிலையத்தில் ஒப்பந்தத்தாரின் வாகனங்கள் எத்தனை எண்ணிக்கையில் பராமரிப்பில் உள்ளன மற்றும் வாகனங்களில் திடக்கழிவுகள் உரக்கிடங்கிற்கு தொய்வின்றி இயக்கப்படுகின்றனவா என்பதனை ஆய்வு செய்தல்
- வாகனத்தின் மூலம் கொண்டு செல்லப்படும் திடக்கழிவுகளின் அளவுகளை ஆய்வு செய்தல்.
- குப்பை மாற்று நிலையத்தில் திடக்கழிவுகளை சேகரிக்கும் பெட்டிகள் போதுமானதா என்பதனை ஆய்வு செய்தல்.
- குப்பை மாற்று நிலையத்தின் எடைமேடை இயந்திரத்தின் அளவீடுகள் மற்றும் உரிமத்தினை ஆய்வு செய்தல்.
- ஒப்பந்ததாரர் ஈரமான (Wet waste) கழிவுகளிலிருந்து உரம் உற்பத்தி செய்யப்படும் முறையை ஆய்வு செய்தல்.
- உரக்கிடங்கிற்கு கொண்டு செல்லப்படும் மொத்த குப்பைகளை தரம் பிரித்து முறைப்படுத்தப்படும் விகிதாச்சாரத்தை ஆய்வு செய்தல்.
- உரக்கிடங்கில் உலர் மற்றும் ஈரமான கழிவுகளை பதப்படுத்தி உரமாக்கும் முறையை ஆய்வு செய்தல்.
- உரக்கிடங்கில் உற்பத்தி செய்யப்பட்ட உரம் மற்றும் துண்டாக்கப்பட்ட பொருள்கள் (RDF) விற்பனையாளருக்கு விற்கப்படுவதை ஆய்வு செய்தல்.

- உரக்கிடங்கின் எடைமேடை இயந்திரத்தின் அளவீடுகள் மற்றும் உரிமத்தினை ஆய்வு செய்தல்.
- திசைநிலை சேகரமாகும் குப்பைகள் அனைத்தும் செயலாக்கத்திற்கு உட்படுத்தப்படுகின்றனவா என்பதை ஆய்வு செய்தல்.
- சிமெண்ட் தொழிற்சாலைக்கு கொண்டு செல்லப்படும் RDF பொருட்களின் அளவுகளை ஆய்வு செய்தல்.
- விண்ரோ உரமாக்கல் (Windrow composting) செயல்முறைக்கு பிறகு கழிவுகள் சோதனை செய்யப்பட்டு Sanitary Landfill (SLF) தளத்தில் (சுகாதார நிலம் நிரப்பும் பகுதி) கொட்டப்படுவதை ஆய்வு செய்தல்.
- உரக்கிடங்கில் கொட்டப்படும் குப்பைகளில் இருந்தும் மற்றும் SLF யில் இருந்தும் வெளிவரும் கசிவுகள் (Leachate) முறையாக கையாளப்படுகின்றனவா என்பதனை ஆய்வு செய்தல்.
- SLF முறையில் கொட்டப்படும் கழிவுகள் கொட்டுவதற்கு முன்பாக முறையாக அறிவியல் ஆய்வு செய்து கொட்டுவதற்கு ஏற்ற குப்பைகள் தான் என்பது உறுதி செய்து செயல்படுத்தப்படுகின்றதா என்பதனை ஆய்வு செய்தல்.
- திடக்கழிவு மேலாண்மை பணிகளுக்காக மேற்கொள்ளப்படும் செலவினங்கள் தொடர்பான அளவுப்புத்தக (M-Book) பட்டியலினை ஆய்வு செய்தல்.
- MSW 2016 விதிகளின் கீழ் சுற்றுச்சூழல் பாதுகாப்பிற்காக நடைமுறைப்படுத்தப்படும் செயல்முறைகளை ஆய்வுசெய்தல்.

இணைப்பு : படிவம்


 ஆணையர்
 கோயம்புத்தூர் மாநகராட்சி

பெறுநர்

1. சம்பந்தப்பட்ட அனைத்து அலுவலர்கள்
கோயம்புத்தூர் மாநகராட்சி

2. M/s. InfraEn India Pvt Ltd, Coimbatore

நகல்

1. அனைத்து மண்டல உதவி ஆணையர்கள்
2. தலைமைப் பொறியாளர் (பொ)
3. துணை ஆணையர் அவர்களுக்கு.
4. துணை மேயர் அவர்களுக்கு
5. ஆணையர் அவர்களின் மேசைக்கு.
6. மாண்புமிகு மேயர் அவர்களுக்கு.


 6/12/24

Proceedings of the Commissioner, Coimbatore City Municipal Corporation,
Coimbatore

Present : M. Sivaguru Prabakaran, I.A.S.

Roc. No. 2185/2024/MC3

Dated : 11.12.2024

Sub : Work order - Coimbatore Corporation -Regarding the issuing of a revised order to investigate the vermicomposting work being done at the Vellalore compost yard and assign work to the officers to submit report.

Ref : This authority dated the same process order dated 02.12.2024

Order:

As per the instructions from the Municipal Commissioner, the Coimbatore City Municipal Corporation has decided to improve the functioning of the vermi compost unit in the Vellalore Solid Waste Management Plant. A Vermi Compost Committee has been formed to oversee operations, ensure proper waste segregation, and improve efficiency.

S. No	Name & Designation	Contact Number
1	K. Arumugam, Zonal Officer (South)	7418920777
2	K. Ramesh, Deputy Commissioner (Health)	9443799211
3	S. Murugan, Assistant Engineer (Vellalore)	9894764574
4	R. Rajkumar, Health Inspector	9443799204
5	G. Ravi, Junior Engineer	9442104124
6	B. Senthil, Supervisor	9443799207
7	K. Prakash, Environmental Engineer	9443799204
8	S. Kumar, Senior Assistant	9489205605
9	R. Venkatesan, Supervisor	9443799216
10	M. Saravanan, Supervisor	9443799212
11	K. Raju, Technical Assistant	9443799211
12	P. Karthik, Junior Engineer	9443799203
13	S. Karthik, Compost Plant Supervisor	9865897150

14	E.Vijayakumar, Deputy Engineer, SBM	9442104137
15	Arunachalam, Deputy Engineer (Vellalore), Central Zone	9442104151
16	S. Arumugam, Deputy Engineer (Vellalore), South Zone	9442104144
17	R. Krishnan, Assistant Health Officer	9449120675

It is directed that the above officers should examine whether the Vermicompost production works are being implemented properly in the Vellalore Compost yard and submit the report to the Commissioner through the Deputy Commissioner after examining the M-Book, list related to the expenses incurred for the Vermicompost production works.

For the Commissioner,
Deputy Commissioner,
Coimbatore City Municipal Corporation.

To,

All officers concerned,
Coimbatore

**Proceedings of the Commissioner, Coimbatore City Municipal Corporation,
Coimbatore**

Present : M. Sivaguru Prabakaran, I.A.S.

Roc. No. 2415/2024/MC7

Dated : 06.12.2024

Thiruvalluvar Year 2055 / Krodhi / Karthikai – 20

Sub : Coimbatore Municipal Corporation Solid Waste Management Plan - Review of the work carried out by Concessionaire BEIL-UPL SPV: M/s. Coimbatore Integrated Waste Management Co. Pvt. Ltd. (CIWMCPL) regarding the collection of daily solid waste in the municipal areas - Forming and Ordering a Solid Waste Management Committee - Regarding

Order:

In the Coimbatore Municipal Corporation areas, the daily collected solid waste is transported by vehicle to the garbage transfer stations. From there, it is transported by lorries to the Vellalore compost yard. The waste is sorted by Concessionaire BEIL-UPL (SPV: M/s. Coimbatore Integrated Waste Management Co. Pvt. Ltd. (CIWMCPL)). To oversee this work, a Solid Waste Management Committee is formed under the leadership of the Deputy Commissioner as follows:

Committee Members:

S. No.	Name and Position	Phone Number
1	K. Sivakumar, Deputy Commissioner	7418920777
2	G. Elangovan, Deputy City Engineer	9443799211
3	K. Karuppusamy, Executive Engineer, Central Zone	9443799219
4	A. Mohan, City Health Officer	9443799202
5	K. Boopathy, Assistant City Health Officer	9442104124
6	N. Kumaran, Assistant Commissioner, South Zone	9443799212

7	R. Ezhil, Assistant Executive Engineer, North Zone	9442501792
8	S. Kanagaraj, Assistant Executive Engineer (General), South Zone	9442501794
9	C. Veeran, Health Officer, West Zone	9443754100
10	N. Rajendran, Health Officer, North Zone	9443478727
11	S. Murugan, Health Officer, East Zone	9865897150
12	N. Vijayakumar, Health Officer, SBM	9443111212
13	R. Gunasekaran, Health Officer (General), Central Zone	9442104151
14	M.V. Andiappan, Health Officer (General), South Zone	9442104144

The officers listed in the above table, along with the Assistant Engineer of Solid Waste Management, Coimbatore Municipal Corporation, and M/S. InfraEn India Pvt. Ltd., Coimbatore, are ordered to conduct inspections at the rates specified below to ensure that the company Concessionaire BEIL-UPL [SPV: M/s. Coimbatore Integrated Waste Management Co. Pvt. Ltd. (CIWMCPL)] is properly implementing solid waste management services as per the terms of their agreement. The inspection reports, completed in the attached forms, should be compiled daily and submitted to the Commissioner through the Deputy Commissioner.

Inspections will focus on:

- Analyzing the waiting time of vehicles arriving at the Transfer Stations with garbage and the reasons for any delays. (This point checks efficiency and potential bottlenecks in the waste disposal process.)
- Verifying the number of vehicles owned and operated by the contractor at the Transfer Stations and ensuring the smooth transport of solid waste to the compost yard without disruptions. (This ensures the contractor has sufficient resources and is operating effectively.)
- Checking the quantity of solid waste transported by vehicles. (This monitors the volume of waste being processed and helps track overall waste management efforts.)

- Checking if the bins at the Transfer Station for collecting segregated waste are sufficient. (This ensures proper waste segregation at the initial stage.)
- Checking the weighbridge readings and license at the Transfer Station. (This verifies the accuracy of weight measurements and regulatory compliance.)
- Analyzing the process used by the contractor to produce compost from wet waste. (This evaluates the composting process for effectiveness and quality.)
- Analyzing the ratio of segregated waste sent to the compost yard from the total waste received. (This monitors the efficiency of the waste segregation process.)
- Analyzing the process of processing and composting dry and wet waste at the compost yard. (Similar to point 6, but broader, covering both dry and wet waste processing.)
- Checking the sale of compost and Refuse Derived Fuel (RDF) produced at the compost yard to vendors. (This checks the final disposal or utilization of the processed waste materials.)
- Checking the weighbridge readings and license at the compost yard. (This ensures accurate weight measurements and regulatory compliance at the final processing site.)
- Verifying that all daily collected garbage is processed. (This checks if the collected waste is actually being processed and not left unattended.)
- Analyzing the quantity of Refuse Derived Fuel (RDF) sent to the cement factory. (This monitors the output and disposal of RDF, a fuel derived from waste.)
- Checking if the waste is properly disposed of at the Sanitary Landfill (SLF) site after the Windrow composting process and verifying proper procedures are followed. (This ensures environmentally sound disposal of remaining waste after composting.)

- Analyzing whether leachate (liquid that drains from landfills) from the compost yard and SLF is being handled properly. (This is crucial for preventing water and soil contamination.)
- Verifying that the waste dumped in the SLF is scientifically analyzed before disposal to ensure it is suitable for landfill disposal. (This ensures only appropriate waste goes into the landfill.)
- Checking the Measurement Book (M-Book) entries related to expenditures incurred for solid waste management activities. (This audits the financial aspects of the solid waste management operations.)
- Verifying the implementation of environmental safeguards under the MSW 2016 rules. (This ensures compliance with environmental regulations related to municipal solid waste management.)

Attachment: Form (Likely refers to the inspection report form mentioned earlier.)

Commissioner,
Coimbatore Municipal Corporation.

To:

1. All Concerned Officers, Coimbatore Municipal Corporation
2. M/s. InfraEn India Pvt Ltd, Coimbatore

Copy to:

1. All Zonal Assistant Commissioners
2. Chief Engineer (General)
3. Deputy Commissioner
4. Deputy Mayor
5. To the Commissioner's table
6. Hon'ble Mayor

Site inspection on 22nd December 2024

Site inspection in Vellalore Compost Yard



Site inspection in CIWMCPL Plant, Vellalore Compost Yard



Coimbatore City Municipal Corporation

From,
Thiru. M.Sivaguru Prabakaran, I.A.S.,
Commissioner
Coimbatore Municipal Corporation,
Big Bazaar Street, Townhall
Coimbatore – 641 001.



To,
M/s. Bhairav Renderers,
C/o. A, Kare Gowder Layout,
Kalveerampalayam,
Coimbatore – 641 046

Roc No. 12404/20202/(ME8)/JN3

Dated: 24.12.2024

Show Cause Notice issued

Sir,

Sub : Coimbatore Municipal Corporation Solid Waste Management – Site Inspection – Public Grievances – Notice Issued for Submission Documents & Instruction to implementation of Odor control measures at Chicken Waste Rendering Processing Facility at Vellalore - Regarding.

Ref : 1) Public grievances raised for order issues on 21.12.2024
2) Inspection dated 22.12.2024

With reference to the site inspection and the grievances received from the public, hereby it is instructed to submit the following reports/documents immediately.

1. Brief description about the process system carried out in the rendering processing plants.
2. Latest As-built drawing of the facility.
3. Machineries and equipment's used for the plant and all its related supplier documents
4. Daily Waste quantity processed, end product generated/disposed quantity details, sale reports with valid proof.
5. Manpower & Collection vehicle resources utilized for the processing & plant.
6. Brief report about the measures to control odor due to the boiling process.
7. All relevant approval documents from concern authorities.

It is also instructed to implement the following measures immediately.

1. Selected native trees plantation as natural odor cover surrounding the facility.
2. Stop operations during night hours.
3. Proposal to improvise the plant operations and to develop an odor less processing facility.
4. Implement/install advanced bio-filter technology or utilize advanced potent liquid neutralizing agent designed to eliminate strong odors at rendering plants.

You are hereby instructed to submit the above said reports and required measures to control the odor. Failing which may result in serious actions.


Commissioner,

Coimbatore City Municipal Corporation.

88
23/12/24

Coimbatore City Municipal Corporation

From,
Thiru. M.Sivaguru Prabakaran, I.A.S.,
Commissioner,
Coimbatore Municipal Corporation,
Big Bazaar Street, Townhall
Coimbatore – 641 001.



To,
M/s. Coimbatore Integrated
Waste Management Co. Pvt. Ltd.,
2-A, Kansas Apartment, Civil
Aerodrome Post, SITRA,
Coimbatore - 641 021.

Roc No. 13385/09/JN3

Dated: 24.12.2024

Sir,

Show Cause Notice issued

Sub : Coimbatore Corporation - Integrated Solid Waste Management
Project: Site Inspection Report – Action to be taken to Control odor
issues – Public grievances – Regarding.

Ref : 1) Public grievances raised for order issues on 21.12.2024
2) Inspection dated 22.12.2024

This is to bring to your attention the findings from the site inspection conducted on 22/12/2024, regarding the operational activities at your waste management facility. The inspection was initiated in response to public grievances concerning odor and related issues at the site.

Following is the list of Observations during the Inspection

Observations

1. **Stagnation of Leachate:** Leachate was found stagnating at multiple locations, indicating inadequate management.
2. **Improper Leachate Management:** There was no proper mechanism observed for the collection, treatment, or disposal of the leachate generated within the plant area.
3. **Unprocessed Waste:** A large stack of unprocessed waste is found accumulating at the site, contributing to the odor and environmental concerns.
4. **Inadequate Odor Control:** No significant efforts were observed to mitigate the odor. Methods like spraying lemongrass or other odor-neutralizing agents were not being implemented effectively.

5. **Processing Time Limit:** It was noted that CCMC has instructed to halt processing activities after 6 PM to avoid odor concerns of the residents
6. **Daily Waste Processing:** The concessionaire must ensure that all waste received is processed daily without delay.
7. **Groundwater Monitoring:** Regular monitoring of groundwater quality in and around the facility must be initiated to detect potential contamination.

Instructions for Immediate Compliance

You are hereby instructed to address the above issues and implement corrective measures on a priority basis. Specifically:

- Clear stagnated leachate and establish a robust leachate management system.
- Process all unprocessed waste and ensure no waste backlog.
- Implement odor control measures immediately, including spraying neutralizing agents such as lemongrass through drone's/sprinkler system.
- Install CCTV cameras within 7 days to monitor all plant operations.
- Ensure daily processing of waste and submit daily reports to CCMC.
- Initiate groundwater monitoring and submit monthly reports.

Follow-Up and Reporting

This Show Cause is issued to submit a compliance report on the above points by **31.12.2024**. Non-compliance will result in further action as per the terms of the Concession Agreement.

We trust that you will take these matters seriously and act promptly to address the grievances and ensure smooth operations at the facility.



Commissioner,
Coimbatore City Municipal Corporation.

88
23/12/24

Coimbatore City Municipal Corporation

From,
Thiru. M.Sivaguru Prabakaran, I.A.S.,
Commissioner
Coimbatore Municipal Corporation,
Big Bazaar Street, Townhall
Coimbatore – 641 001.



To,
M/s. Nila Blooms Scappes and
Decors,
286, Kandasamy Layout,
Pappanaickenpalayam,
Coimbatore - 641037

Roc No. 6951/22/(MD4) /JN3

Dated: 24/12.2024

Show Cause Notice issued

Sir,

Sub : Coimbatore City Municipal Corporation - Integrated Solid Waste Management Project: Site Inspection Report – Action to be taken to Control odor issues – Public grievances – Regarding.

Ref : 1) Public grievances raised for order issues on 21.12.2024
2) Inspection dated 22.12.2024

This is to bring to your attention the findings from the site inspection conducted on 22/12/2024, regarding the operational activities at your waste management facility. The inspection was initiated in response to public grievances concerning odor and related issues at the site.

Following is the list of Observations during the Inspection

Observations

1. **Stagnation of Leachate:** Leachate was found stagnating at multiple locations, indicating inadequate management.
2. **Improper Leachate Management:** There was no proper mechanism observed for the collection, treatment, or disposal of the leachate generated within the plant area.
3. **Unprocessed Waste:** A large stack of unprocessed waste is found accumulating at the site, contributing to the odor and environmental concerns.
4. **Inadequate Odor Control:** No significant efforts were observed to mitigate the odor. Methods like spraying lemongrass or other odor-neutralizing agents were not being implemented effectively.

5. **Processing Time Limit:** It was noted that CCMC has instructed to halt processing activities after 6 PM to avoid odor concerns of the residents
6. **Daily Waste Processing:** The concessionaire must ensure that all waste received is processed daily without delay.
7. **Groundwater Monitoring:** Regular monitoring of groundwater quality in and around the facility must be initiated to detect potential contamination.

Instructions for Immediate Compliance

You are hereby instructed to address the above issues and implement corrective measures on a priority basis. Specifically:

- Clear stagnated leachate and establish a robust leachate management system.
- Process all unprocessed waste and ensure no waste backlog.
- Implement odor control measures immediately, including spraying neutralizing agents such as lemongrass through drone's/sprinkler system.
- Install CCTV cameras within 7 days to monitor all plant operations.
- Ensure daily processing of waste and submit daily reports to CCMC.
- Initiate groundwater monitoring and submit monthly reports.

Follow-Up and Reporting

This Show Cause is issued to submit a compliance report on the above points by **31/12/2024**. Non-compliance will result in further action as per the terms of the Concession Agreement.

We trust that you will take these matters seriously and act promptly to address the grievances and ensure smooth operations at the facility.


Commissioner,
Coimbatore City Municipal Corporation.

88
23/12/24

Coimbatore City Municipal Corporation

From,
Thiru. Sivaguru Prabakaran I.A.S
Commissioner
Coimbatore City Municipal Corporation,
Big Bazaar Street, Townhall,
Coimbatore – 641 001.



To,
M/s. Coimbatore Integrated Waste
Management Company Pvt. Ltd.,
2-A, Kansas Apartment,
Civil Aerodrome Post,
SITRA, Coimbatore - 641 021.

Roc No. 13385/2006/JN3

Dated: 25.10.2024

Sir,

Sub: Coimbatore Corporation – Solid Waste Management - Unauthorized Discharge of Untreated Leachate and Non-compliance with Solid Waste Management Rules, 2016 - Non-maintenance of Leachate Treatment facility- Show Cause Notice – Issued - Regarding.

Ref: Concession Agreement dated 19-11-2007

This Notice of Show Cause is issued as a formal warning regarding the unauthorized discharge of untreated leachate through an unapproved pipe outlet from M/s CIWMCPL's boundary wall into neighboring property, and the inadequate treatment and management of leachate from the landfill under your operational control. This constitutes a direct violation of the Solid Waste Management Rules, 2016, and relevant provisions of the CPCB and TNPCB guidelines as mandated under the Environmental Protection Act, 1986.

During a recent inspection conducted on October 17, 2024, between 2:30 p.m. and 3:30 p.m., it was discovered that leachate from your operational area was overflowing into adjacent land (an abandoned plot designated for the New Bus Terminal) via an unauthorized pipeline originating from your compound's boundary wall, in contravention of the approved construction plan. This not only constitutes an illegal discharge but also violates the terms of the Concession Agreement.

Furthermore, the leachate is neither being treated nor managed in accordance with the guidelines set forth in Rule 15 and Rule 22 of the Solid Waste Management Rules, 2016. Site Photographs dated 18th October, 2024, showing the

illegal pipe connection from M/s CIWMCPL boundary wall compound jutting into the abandoned land reserved for construction of New Bus Stand (neighboring property) is enclosed with this letter as reference.

These rules clearly stipulate the following requirements:

1. Leachate Management: Leachate must be properly collected and treated using appropriate methods before discharge, as mandated by Rule 15(zi), Rule 22(4), and Rule 22(5) of the Solid Waste Management Rules, 2016. Your failure to maintain and operate the Leachate Treatment Plant (LTP) has resulted in serious environmental harm.

2. Emergency Preparedness: It was observed that no emergency measures were implemented during the heavy rainfall on October 14th, 15th, and 16th, 2024, leading to a leachate overflow. There were no contingency plans in place to prevent the accidental discharge of leachate into adjacent land.

The SWM Rules, 2016, and TNPCB guidelines clearly state that untreated leachate poses a significant risk to surrounding groundwater and surface water resources, including rivers, lakes, and ponds, thereby threatening aquatic ecosystems and potentially contaminating water used for agriculture.

3. Breach of the Environmental Protection Act, 1986: Failure to treat and safely discharge leachate also constitutes a breach of the Environmental Protection Act, 1986. The Act mandates that hazardous liquid waste must not contaminate soil, water bodies, or groundwater. Any violation of this may lead to punitive action under Section 15 of the Act, which could result in legal penalties.

Despite your consistent claims that the LTP is fully operational, it has come to light that untreated leachate has been discharged into open adjoining land through an unauthorized outlet. You have failed to produce a Wastewater Quality Report and have not adhered to the Leachate Management Parameters.

Given the severe environmental risks posed by the illegal discharge of untreated leachate, including groundwater contamination, surface water pollution, and soil degradation, you are hereby directed to take the following corrective actions

immediately to ensure compliance with the SWM Rules, 2016, and the Environmental Protection Act, 1986:

- Ensure that the Leachate Treatment Plant is fully operational and that the leachate collection and treatment systems comply with all prescribed guidelines.
- Immediately treat the leachate that has accumulated in the adjoining premises and manage its reuse in a scientifically sound manner.
- Regularly monitor and report on water quality to prevent any future illegal discharges.


Failure to address these deficiencies within 10 days from the receipt of this notice will result in necessary legal action, including but not limited to, termination of the Concession Agreement and the imposition of penalties as prescribed by law.

Please be informed that due to the gross negligence and illegal actions of discharging untreated leachate through an unauthorized outlet from M/s CIWMCPL's boundary wall, resulting in significant environmental and social risks, M/s CIWMCPL will be held solely responsible for all consequences.

Your immediate compliance and response within the specified timeline are expected, failing which a penalty will be imposed and recovered from you as per the applicable legal provisions.

Encl.: Site Photographs

Commissioner,
Coimbatore City Municipal Corporation.



Handwritten signatures and dates in blue ink:

- Top left: A signature and the date '21/10/24'.
- Top right: A signature and the date '21/10/24'.
- Bottom left: A signature and the date '21/10/24'.
- Bottom center: A signature and the date '21/10/24'.
- Bottom right: A signature and the date '21/10/24'.

Leachate Discharged from CIWMCP – Site Photography – Dated : 18.10.2024

	
<p>Leachate Pond behind Vellalore Bus Stand</p>	<p>CIWMCP Boundary Wall</p>
	
<p>Discharge pipe</p>	<p>Illegal Discharge pipe from CIWMCP</p>
	
<p>Leachate Pond behind Vellalore Bus Stand</p>	<p>Leachate Pond behind Vellalore Bus Stand</p>

Spraying of disinfectant and Lemon grass solutions in Processing Plant



Spraying of disinfectant and Lemon grass solutions in CIWMCPL Plant



Spraying of disinfectant and Lemon grass solutions in Vermi Compost Plant




CCMC has planted about 5000 saplings in the compost yard



Plantation in Vellalore Compost Yard



Plantation in Vellalore Compost Yard

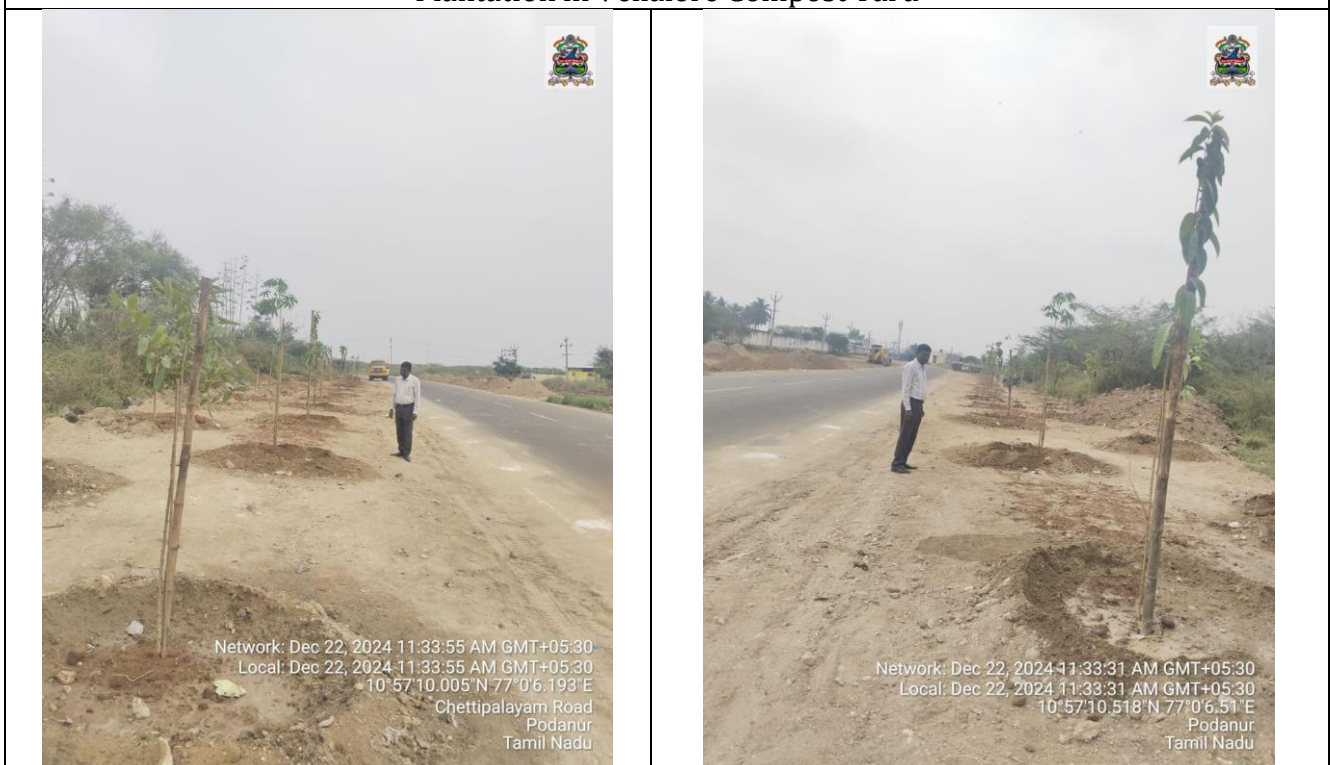

Natural Solution spraying using a drone at the Vellalore compost yard



Natural solution spraying work in Vellalore compost yard




Natural solution spraying work in Vellalore compost yard



Drone View of Natural solution spraying work in Vellalore compost yard



*Area Covered by Drone Spraying is marked in Green Color – Vellalore Compost Yard Odor Control Efforts by CCMC

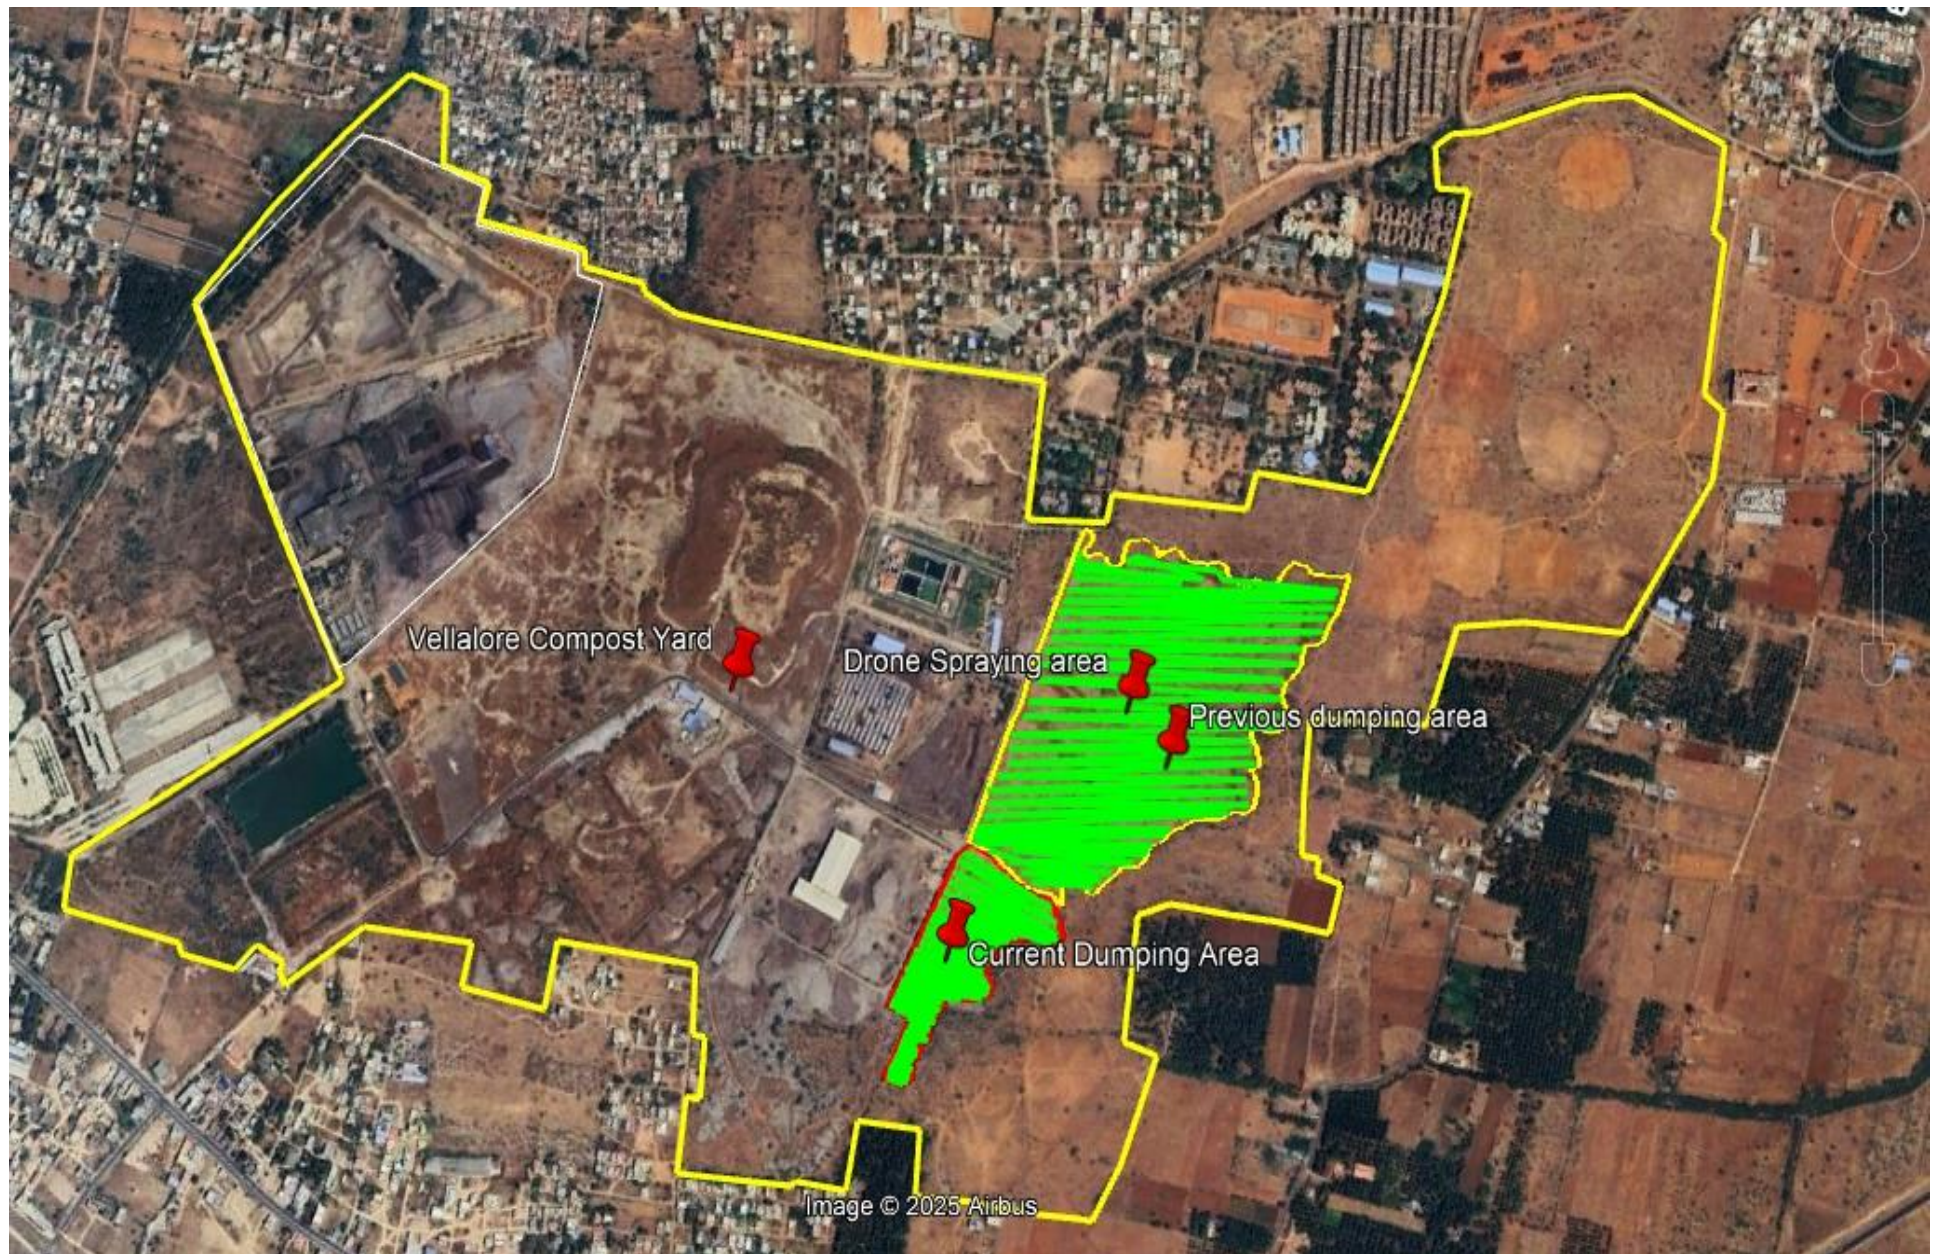

Coimbatore City Municipal Corporation

From,
Thiru. Sivaguru Prabakaran I.A.S
Commissioner,
Coimbatore City Municipal Corporation,
Big Bazaar Street, Townhall,
Coimbatore – 641 001.



To,
M/s. Coimbatore Integrated Waste
Management Company Ltd.,
2-A, Kansas Apartment,
Civil Aerodrome Post, SITRA,
Coimbatore - 641 021.

Roc No. 13385/09/JN3

Dated: .11.2024

Sir,

Sub: Coimbatore Corporation – Solid Waste Management- Show Cause Notice- Unauthorized Discharge of Untreated Leachate and Non-compliance with Solid Waste Management Rules, 2016- Non-maintenance of Leachate Treatment facility and imposing of penalty Rs. 50,00,000/- – Regarding.


- Ref: 1) Concession Agreement between CCMC & BEIL-UPL dated 19.11.2007.
2) This office letter Roc. No. 13385/0/JN5, dated 25.10.2024.
3) Your letter Ref. No. CIWMCPL/CCMC/04/085/2024-25 dated 09.11.2024.

The explanation to the show cause notice from this office, dated 25.10.2024 are baseless and unsubstantiated and contains a series of inaccurate and misleading statements that not only misrepresent the facts but also cast aspersions on the integrity of our investigation. The irrefutable evidence and assertions regarding the origin of the pipelines and the lack of responsibility for leachate seepage are found to be true. The concrete evidence produced in the Annexure and your complete denial of responsibility for the environmental impact of your operations is unacceptable.

The explanation offered by you have been examined by our officers who had done a fact finding and a joint inspection carried out along with public & elected representatives at the specified location and found that Leachate flowing out from your boundary wall and it was verified that the untreated Leachate has accumulated due to the lapse of proper maintenance, not only of the Leachate Treatment Plant (LTP) but no preventive measures were taken to stop the Leachate entering into the neighboring property from your processing facility.

Under explanation was found unsatisfactory and contrary to the facts. In fact and circumstances of the case, a fine of Rs.50,00,000/- is imposed.

Furthermore, you are directed to submit your action plan to reclaim the affected neighboring property within 10 days of the letter dated.


Commissioner,
Coimbatore City Municipal Corporation.

806
25/11/24



COIMBATORE CITY MUNICIPAL CORPORATION

Tender Notice No.e66/2024

Date 23.12.2024

Coimbatore Corporation

(Two Cover System-e-submission only) File No.3382/2024/ JN3

1. Bids are invited Removal of legacy waste through Bio/ Mining process at Vellalore dump yard in Coimbatore city municipal corporation (7,94,139 MT).
2. Total Estimate Amount Rs.5854.00 Lakhs.
3. The bid documents can be downloaded from the website <https://tntenders.gov.in> free of cost.
4. Amount of Earnest Money Deposit will be 1% of the estimated value of work.
5. Any additional/further details and conditions related to these works can be had from the office of the Commissioner, Coimbatore City Municipal Corporation.

6. Important dates

1.	Date and time of Pre Bid Meeting	07.01 .2025 at 11.00 A.M
2.	Last Date and time for downloading bid documents	27.01.2025 at 3.00 P.M
3.	Last Date and time for submission of bid document online e-submission only	27.01.2025 at 3.00 P.M
4.	Date and time of opening of the Technical Bids	28.01.2025 at 4.00 P.M
7.	In the event of the specified date for submission of bids is declared as a holiday, bids will be received and opened on the next working day at the same time.	
8.	Commissioner, Coimbatore Corporation, Big Bazaar Street, Townhall, Coimbatore-641001, Ph.No.0422-2396026, E-mail commr.coimbatore@tn.gov.in	

COMMISSIONER,
COIMBATORE CORPORATION

DIPR/5598/TENDER/2024

Air
Ne
Por

கோவை மாவட்டத்தி் குகளில் எண்ணிக்கையை உள்ளது. பற்றப்பால் துறையினரால் கட்டப்பட்டது.

மாத்தி யோசிக்கிறாங்க!

கழிவு நீரை சுத்திகரித்து மறுபயன்பாட்டுக்கு வழங்குவதற்கு... மாநகராட்சியில் ரூ.245 கோடிக்கு செயல்படுத்த கமிஷனர் திட்டம்

கோவை, ஜன. 7- “கோவை மாநகராட்சி பகுதியில் வெளியேற்றப்படும் கழிவு நீரை சுத்திக்க, ரூ.245 கோடி ஒதுக்கி, தமிழக அரசு நிர்வாக அனுமதி வழங்கியுள்ளது,” என, மாநகராட்சி கமிஷனர் சிவசுக்கு பிரபாகர் தெரிவித்தார்.

“இனாமஸ்” நாளிதழுக்கு, அவர் அளித்த நிறப்பு பேட்டியில் கூறியதாவது:

கோவையில் சுத்திகரிப்பு நிலையங்களில், சுத்திகரித்த கழிவு நீர் மீண்டும் ஒரு முறை சுத்திகரித்து, தொழிற்சாலை பயன்பாட்டுக்கு வழங்கப்படும். நானொன்றுக்கு, 2.8 கோடி லிட்டர் கழிவு நீரை சுத்திக்க, 245 கோடி ரூபாய்க்கு தமிழக அரசிடம் நிர்வாக அனுமதி பெறப்பட்டிருக்கிறது.

புதிதாக பொதுக்கழிப்பிடங்கள்

- பொது சுகாதாரத்தை பேணிக்காக்க, தேவைப்படும் இடங்களில் பொதுக்கழிப்பிடங்கள் புதிதாக கட்டப்படவுள்ளன. செயல்பாட்டில் இருப்பது புதுப்பிக்கப்படும். பராமரிப்பு பணி மேற்கொள்ள ரூ.400 கோடிக்கு மதிப்பீடுதயாரித்துள்ளோம்.
- விடுபட்ட பகுதிகளில், குடிநீர் சப்ளை செய்ய, திட்ட அறிக்கை தயாரித்து வருகிறோம்; 130 கோடி ரூபாய் தமிழக அரசு ஒதுக்க இருக்கிறது. குறிச்சி, குளியமுத்துாரில் விடுபட்ட இடங்களில் குடிநீர் வினியோகிக்க, 5.5 கோடி ரூபாயில் பணிகள் நடந்து வருகின்றன.

தொட்டிகளுக்கு தண்ணீர்

- வடக்கு, கிழக்கு மண்டலங்களில், 59 தொட்டிகள், மேற்கு மண்டலத்தில், 31 தொட்டிகளுக்கு தண்ணீர் தருவிக்க

ஏற்பாடு செய்து வருகிறோம். இதில், 9 தொட்டிகளை பயன்பாட்டுக்கு கொண்டு வந்து லிட்டோம்; 55 ஆயிரம் இணைப்புகள் வழங்க வேண்டும்; இதுவரை எட்டாயிரம் புது இணைப்புகள் வழங்கி, தண்ணீர் கொடுத்து வருகிறோம்; மூன்று மாதத்துக்குள் அனைத்து இணைப்புகளும் வழங்கி விடுவோம். மேற்கு மண்டலத்தில், 22 ஆயிரம் இணைப்பு கொடுக்க வேண்டும்.

17 ஆயிரம் இணைப்பு வழங்கியுள்ளோம். ஒரு மாநகருக்குள் மீதமுள்ள ஐந்தாயிரம் இணைப்பு வழங்கி, புது தொட்டிகளை பயன்பாட்டுக்கு கொண்டு வருவோம். 24 மணி நேர குடிநீர் திட்ட பணி இவ்வாண்டு இறுதிக்குள் முடிக்கப்படும்.

குளங்கள் மேம்பாடு

- சிங்கநல்லூர் குளத்தை மேம்படுத்த, தனி திட்ட அறிக்கை தயாரிக்க உள்ளோம். சின்ன

வேடம்பட்டி குளத்தில் எப்போதும் தண்ணீர் தேக்கமிருப்பது போல் திட்டம் தயாரித்துள்ளோம்; குளம் தூர்வாரப்பட்டு தயாராக இருக்கிறது; இதுவரை தண்ணீர் வரவில்லை. தண்ணீரை கொண்டு வர திட்டமிட்டுள்ளோம். சுத்திகரிப்பு நிலையம் கட்டி, மாகக்கட்டுப்பாட்டு வாரிய விதிமுறைப்படி, சுத்திகரித்து, குளத்தில் தேக்கப்படும். கொய்யல் ஆற்றை அளவீடு செய்து, மேம்படுத்தப்படும்.

நீர் நிலைகளுக்கு, தண்ணீர் வரும் வழித்தடங்களில் இருந்து தடைகளை அகற்றி வருகிறோம். இனி, கழிவு நீர் வராத அளவுக்கு ஆய்வு செய்து விரிவான திட்ட அறிக்கை தயாரித்து ருக்கிறோம். அரசின் ஒப்புதலுக்கும், நிதி ஒதுக்கீட்டுக்கும் அனுப்பியுள்ளோம். இவ்வாறு, கமிஷனர் கூறினார்.

சூரிய ஒளியில் மின்னுற்பத்தி

கமிஷனர் சிவசுக்கு பிரபாகர் கூறியதாவது: 150 கோடி ரூபாய் மதிப்பீட்டில், 20 மெகாவாட் சூரிய ஒளி மின்னுற்பத்தி நிலையம் வெள்ளலூரில் அமைய இருக்கிறது. செம்மொழி பூங்கா பணிகள், 60 சதவீதம் முடிந்திருக்கிறது; 2.5 லட்சம் செடிகள் நடப்போகிறோம். அதில், 30 ஆயிரம் செடிகள் நரும் பணி நடந்து வருகிறது. நமது மாநிலத்தின் பாரம்பரிய, அரிய வகை செடிகளாக அறியப்பட்ட, 512 செடிகள் கண்டறியப்பட்டு, அவற்றின் விதைகள் சேகரித்து, முளைக்க வைத்து, செடிகளாக நட்டு வருகிறோம். ஒவ்வொரு செடியின் வரலாறு தொடர்பாக, மக்கள் அறியும் வகையில் பலகை மற்றும் ‘க்யூஆர்’ கோடு வைக்கப்படும்.



‘குப்பையில் கான், மின்சாரம்’

‘ரூ.65.79 கோடியில் ‘பியோகான்’ திட்டம் செயல்படுத்துவதற்கான பணிகள் நடந்து வருகின்றன; கோர்ட்டில் தொடர்புபட்டுள்ள வழக்கில் தீர்ப்பு பெறப்பட்டு, இப்பணி மேற்கொள்ளப்படும். 600 டெட்ரிக் டன் குப்பையில் மின்சாரம் தயாரிக்கும் திட்டம் செயல்படுத்த உள்ளோம். மாநகராட்சியோடு அருகாமையில் உள்ள என்எச்அமைப்புகளை இணைத்து செயல்படுத்தப்படும். இதுகாண விரிவான திட்ட அறிக்கை, இரு வாரத்தில் தயாராகி விடும். குப்பையில் கான் தயாரிக்கும் திட்டம்; மின்சாரம் தயாரிக்கும் திட்டம் பயன்பாட்டுக்கு வந்து விட்டால், கிடங்கிற்கு குப்பை செல்லாமல் தவித்து விடலாம். இவ்வாறு, அவர் கூறினார்.

Construction / Revamp of Sathy Road Transfer Station



Construction Revamped Sathy Road Transfer Station



Construction Revamped Sathy Road Transfer Station



Municipal Administration and Water Supply Department

From

M.SivaguruPrabakaran, I.A.S.,
Commissioner
Coimbatore City Municipal
Corporation,
Coimbatore – 641 001



To

M/s.Parishudh Ventures
79, 1STMain,Mico Layout,
BTM 2nd Stage,
Bengaluru-560076

Roc.No :7199/2024/JN5

dated 31.12.2024

Letter of Acceptance

Sir,

Sub: Coimbatore Corporation -" Construction of Transfer Station for Coimbatore Corporation at the Location near Kovaipudur with a capacity of 200 TPD , South Zone under **SBM 2.0 – Estimate Amount Rs.9.96 Cr -Letter of Acceptance** – intimation -regarding.

Ref: 1. Tender e43/2024 dated 26.11.2024
2. Finance Bid Opening on 13.12.2024
3. Tender Scrutiny Committee Approved dated. 26.12.2024

This is to notify that your financial bid dated 13.12.2024, to be read in conjunction with your work proposal for "Construction of Transfer Station for Coimbatore Corporation at the Location near Kovaipudur with a capacity of 200 TPD , South Zone under **SBM 2.0** , has been recommended by the Committee. Accordingly, the contract value of **Rs.9,50,20,211.25 /-** which is 0.18% less than the tender value, is accepted, inclusive of GST, etc.,

You are hereby required to furnish a Performance Security of 2% of the contract value. Since you have already paid 1% of the estimated value as Earnest Money Deposit (EMD), this amount will be treated as part of the Performance Security. Therefore, you are required to submit an additional 1% of the contract value, rounded off to Rs. 9,50,300 (Rupees Nine Lakh Fifty Thousand Three Hundred only), in the form of a Bank Guarantee or Demand Draft from an Indian Scheduled/Nationalized Bank within 7 days from the date of receipt of this letter of acceptance.

This is to inform you to sign the Contract Agreement.


**Commissioner,
Coimbatore Corporation.**


30/12/24

Municipal Administration and Water Supply Department

From

M.SivaguruPrabakaran, I.A.S.,
Commissioner
Coimbatore City Municipal
Corporation,
Coimbatore – 641 001



To

M/s.Parishudh Ventures
79, 1STMain,Mico Layout,
BTM 2nd Stage,
Bengaluru-560076

Roc.No : 7197/2024/JN5

dated 31.12.2024

Letter of Acceptance

Sir,

Sub: Coimbatore Corporation -“ Construction of Transfer Station for Coimbatore Corporation at the Location near Peelamedu with a capacity of 200 TPD under **SBM 2.0 – Estimate Amount Rs.9.97 Cr -Letter of Acceptance** – intimation -regarding.

Ref: 1. Tender e43/2024 dated 26.11.2024
2. Finance Bid Opening on 13.12.2024
3. Tender Scrutiny Committee Approved dated. 26.12.2024

This is to notify that your financial bid dated 13.12.2024, to be read in conjunction with your work proposal for “Construction of Transfer Station for Coimbatore Corporation at the Location near Peelamedu with a capacity of 200 TPD under **SBM 2.0**, has been recommended by the Committee. Accordingly, the contract value of **Rs.9,51,58,618.76 /-** which is 0.25% less than the tender value, is accepted, inclusive of GST, etc.,

You are hereby required to furnish a Performance Security of 2% of the contract value. Since you have already paid 1% of the estimated value as Earnest Money Deposit (EMD), this amount will be treated as part of the Performance Security. Therefore, you are required to submit an additional 1% of the contract value, rounded off to Rs.9,51,600 /-(**Rupees Nine Lakh and Fifty Thousand and Six Hundred Only**)in the form Bank Guarantee/Demand Draft from an Indian Scheduled / Nationalized Bank within 7 days from the date of receipt of this letter of acceptance.

This is to inform you to sign the Contract Agreement.


**Commissioner,
Coimbatore Corporation.**


30/12/24

Municipal Administration and Water Supply Department

From

M.SivaguruPrabakaran, I.A.S.,
Commissioner
Coimbatore City Municipal
Corporation,
Coimbatore – 641 001



To

M/s.Parishudh Ventures
79, 1STMain,Mico Layout,
BTM 2nd Stage,
Bengaluru-560076

Roc.No : 7198/2024/JN5

dated 31.12.2024

Letter of Acceptance

Sir,

Sub: Coimbatore Corporation -" Construction of Transfer Station at Kavundapalayam With a Capacity of 200 TPO for the Coimbatore Corporation. under SBM 2.0 – **Estimate Amount Rs.9.99 Cr -Letter of Acceptance** – intimation -regarding.

Ref:

1. Tender e43/2024 dated 26.11.2024
2. Finance Bid Opening on 13.12.2024
3. Tender Scrutiny Committee Approved dated. 26.12.2024

This is to notify that your financial bid dated 13.12.2024, to be read in conjunction with your work proposal for "Construction of Transfer Station at Kavundapalayam With a Capacity of 200 TPO for the Coimbatore Corporation. under SBM 2.0 has been recommended by the Committee. Accordingly, the contract value of **Rs.9,56,43,984.44 /-** which is 0.19% less than the tender value, is accepted, inclusive of GST, etc.,

You are hereby required to furnish a Performance Security of 2% of the contract value. Since you have already paid 1% of the estimated value as Earnest Money Deposit (EMD), this amount will be treated as part of the Performance Security. Therefore, you are required to submit an additional 1% of the contract value, rounded off to Rs.9,56,500 /-(**Rupees Nine Lakh and Fifty Six Thousand and Five Hundred Only**)in the form Bank Guarantee/Demand Draft from an Indian Scheduled / Nationalized Bank within 7 days from the date of receipt of this letter of acceptance.

This is to inform you to sign the Contract Agreement.


**Commissioner,
Coimbatore Corporation.**


30/12/24

Case Details			
Filing No.	WP-170814/2024	Filing Date	13/12/2024
Registration No.	WP-38606/2024	Registration Date	13/12/2024
Stage	Pending		
CNR	HCMA012374522024		
Petitioner and Respondent Details			
Petitioner Details	REFEX GREEN POWER LTD REP BY ITS AUTHORISED SIGNATORY, SECOND FLOOR, REFEX TOWERS ,STERLING ROAD SIGNAL, 313, VALLUVAR KOTTAM HIGH ROAD, NUNGAMBAKKAM, CHENNAI-600 034		
Respondent Details	THE TECHNICAL EVALUATION AND SCRUTINY COMMITTEE TAMILNADU, PRINCIPAL SECRETARY CONFERENCE HALL, MAWS DEPARTMENT, 8TH FLOOR, NKM BUILDING, SECRETARIAT, CHENNAI R-2 DIRCTORATE OF MUNICIPAL ADMINISTRATION GOVERNMENT OF TAMILNADU R-3 THE COMMISSIONER		

	COIMBATORE CITY MUNICIPAL CORPORATION, TOWN HALL, COIMBATORE-641 001 R-4 THE COMMISSIONER MADURAI CITY MUNICIPAL CORPORATION, ARGNAR ANNA MALIGAI, THALLAKULAM, MADURAI-625 002		
Petitioner Counsel	SURYA TEJA SS NALLA AISHWARYA NATHAN TULESH BALAJE R		
Respondent Counsel	DR.T.SEENIVASAN SPECIAL GOVERNMENT PLEADER FOR RESPONDENTS		
Subject	General Miscellaneous		
District	Chennai	Nature of Writ	Certiorarified Mandamus
Case Ready Status	Not Ready		
Coram	HONOURABLE MR JUSTICE S. SOUNTHAR		
Causelist	Regular List	Bench Type	Single Bench

Last Listed on	20/01/2025	Item No.	36
Last return date	13/12/2024	Last Represent date	

History of Case Hearing

Judge	Item no.	Business On Date	Business	Hearing Date	Purpose of hearing	Adjournment
HONOURABLE MR JUSTICE S. S. SUNDAR, HONOURABLE MR.JUSTICE P. DHANABAL				13/12/2024	FOR ADMISSION	
HONOURABLE MR JUSTICE S. SOUNTHAR	1	13/12/2024	INTERIM DIRECTION	18/12/2024	FOR ADMISSION	ADJOURNED
HONOURABLE MR JUSTICE S. SOUNTHAR	40	18/12/2024	TOP OF THE REGULAR LIST	20/12/2024	=====	ADJOURNED
HONOURABLE MR JUSTICE S. SOUNTHAR	4	20/12/2024	DIRECTION.	21/01/2025	~~~~~	ADJOURNED
HONOURABLE MR JUSTICE S. SOUNTHAR	36	20/01/2025	INTERIM ORDER EXTENDED	03/02/2025	=====	ADJOURNED

The comparative tables showing the processed waste quantity and open dumped quantity for Month of Nov 2023 till Dec 2024

Month	Waste quantity Processed (MT)	Open Dumping (MT)	Total Waste (MT)
Nov-23	20,072.11	11,466.14	31,538.25
Dec-23	27,224.15	10,805.46	38,029.61
Jan-24	25,726.33	10,046.61	35,772.94
Feb-24	26,493.48	9,114.09	35,607.57
Mar-24	29,747.09	4,922.86	34,669.95
Apr-24	28,888.02	3,947.35	32,835.37
May-24	30,032.46	3,274.94	33,307.40
Jun-24	27,720.97	3,324.25	31,045.22
Jul-24	27,128.63	3146.8	30,275.43
Aug-24	23,972.80	2,970.06	26,942.86
Sep-24	22,747.80	1,198.15	23,945.95
Oct-24	25,205.40	3,127.50	28,332.90
Nov-24	20,433.60	6,035.43	26,469.03
Dec-24	23,189.40	3,882.19	27,071.59

